


Stewart Mill @ West Stewart Mill & Yancey Roads
DCDOT

ID	Task Name	Duration*	Start	Finish
1	Utility Adjustment			
1.1	GA Power Transmission	449	0	449
1.2	GreyStone Power	29	449	478
1.3	Comcast**	90	478	568
1.4	ATT	224	568	792
1.5	Douglasville-Douglas County WSA	17	612	629
2	Construction			
2.1	Construction Activity (6 Months)	180	612	792

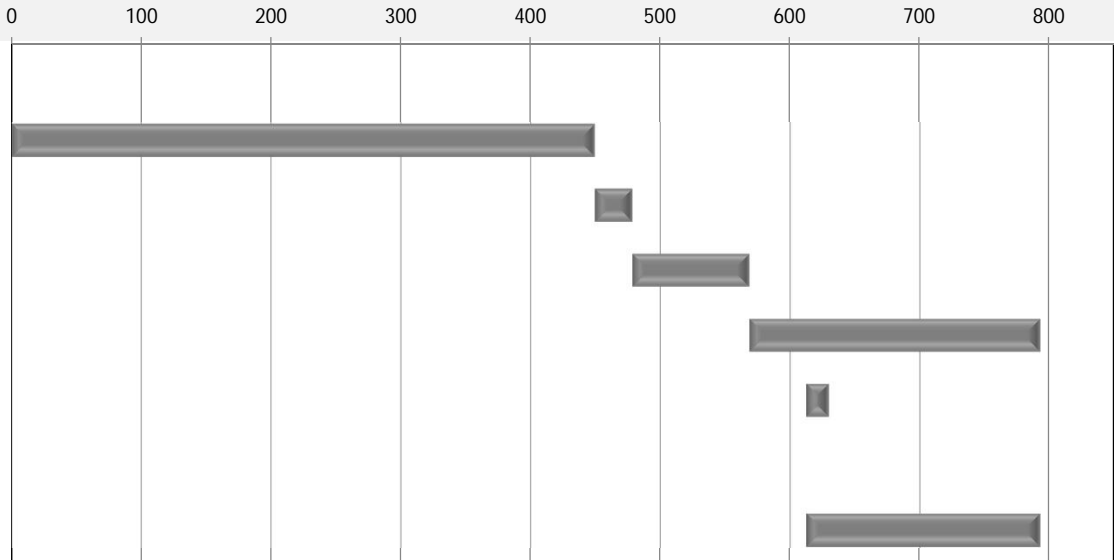

* Calendar Days

** Comcast did not provide UAS this duration is an estimate

Item #	Notes
1.1	GA Power Transmission needs 321 days for utility adjustment this excludes weekends. ADDED 128 days for weekends to be consistent with calendar days
1.2	GreyStone needs 21 days for utility adjustment this excludes weekends. Cannot work until GA Power Transmission pole relocated. ADDED 8 days for weekends to be consistent with calendar days
1.3	Comcast did not provide UAS; estimated 90 days to relocate utilities. This will follow GreyStone.
1.4	ATT needs 160 days for utility adjustment this excludes weekends. This will follow Comcast. ADDED 64 days for weekends to be consistent with calendar days
1.5	WSA needs 13 days for utility adjustment this excludes weekends. Can work concurrently with construction schedule. ADDED 4 days for weekends to be consistent with calendar days
2.1	Total project duration (including Utility Adjustment) = 792 days Note: Contractor can work concurrently during utility adjustment, but the project may be extended due to delay of utility adjustment that affects contractor's critical path items
